

# Progress Report on the Fellowship Hall/Kitchen Renovations

June 26, 2018

Great progress is being made on the Fellowship Hall/Kitchen renovation project this summer. The work started on Monday, May 21, with demolition of the entire area of the interiors of the Fireside Room, the Fellowship Hall and the Kitchen.

Here is a list of the actions that have been completed on schedule in the first five weeks:

1. All interior walls have been skimmed, prime painted, and first coat of paint applied.
2. New ceiling grid is in.
3. Fire protection system is installed and trimmed out.
4. Light fixtures are installed.
5. Fire alarm devices have been re-installed.
6. Trim around the feature wall in the Fireside Room has been modified.

Actions that will be completed in the coming days and weeks:

1. Kitchen hood installation.
2. Fellowship Hall above ceiling inspection with the City of Vestavia Hills.
3. Ceiling tile installation in Fellowship Hall and Fireside Room.
4. Wall skimming touch-up and final coat of paint.
5. Kitchen above ceiling inspection with the City of Vestavia Hills.
6. Lay the carpet in the Fellowship Hall and Fireside Room.
7. Install new sound system.

Our contract calls for us to have the entire area ready for us to occupy by Sunday August 5. The report from the general contractor is that we are on schedule and on budget.

*More information at right; more pictures on pages 2 and 3.*




There is still time for us to do some of the things that we hoped to do but didn't have funding to do. Several members have made donations for us to move forward on a few of these items. If you would like to make a donation to help make more of these items possible, please give now and mark your donation for the Fellowship Hall/Kitchen project.


Lighting and ceiling tile installation



Hallway included in renovation

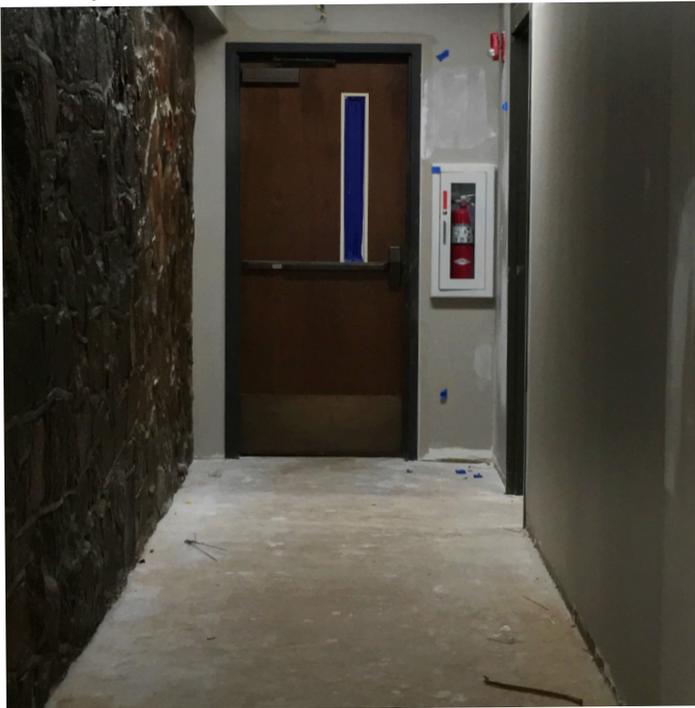

Kitchen

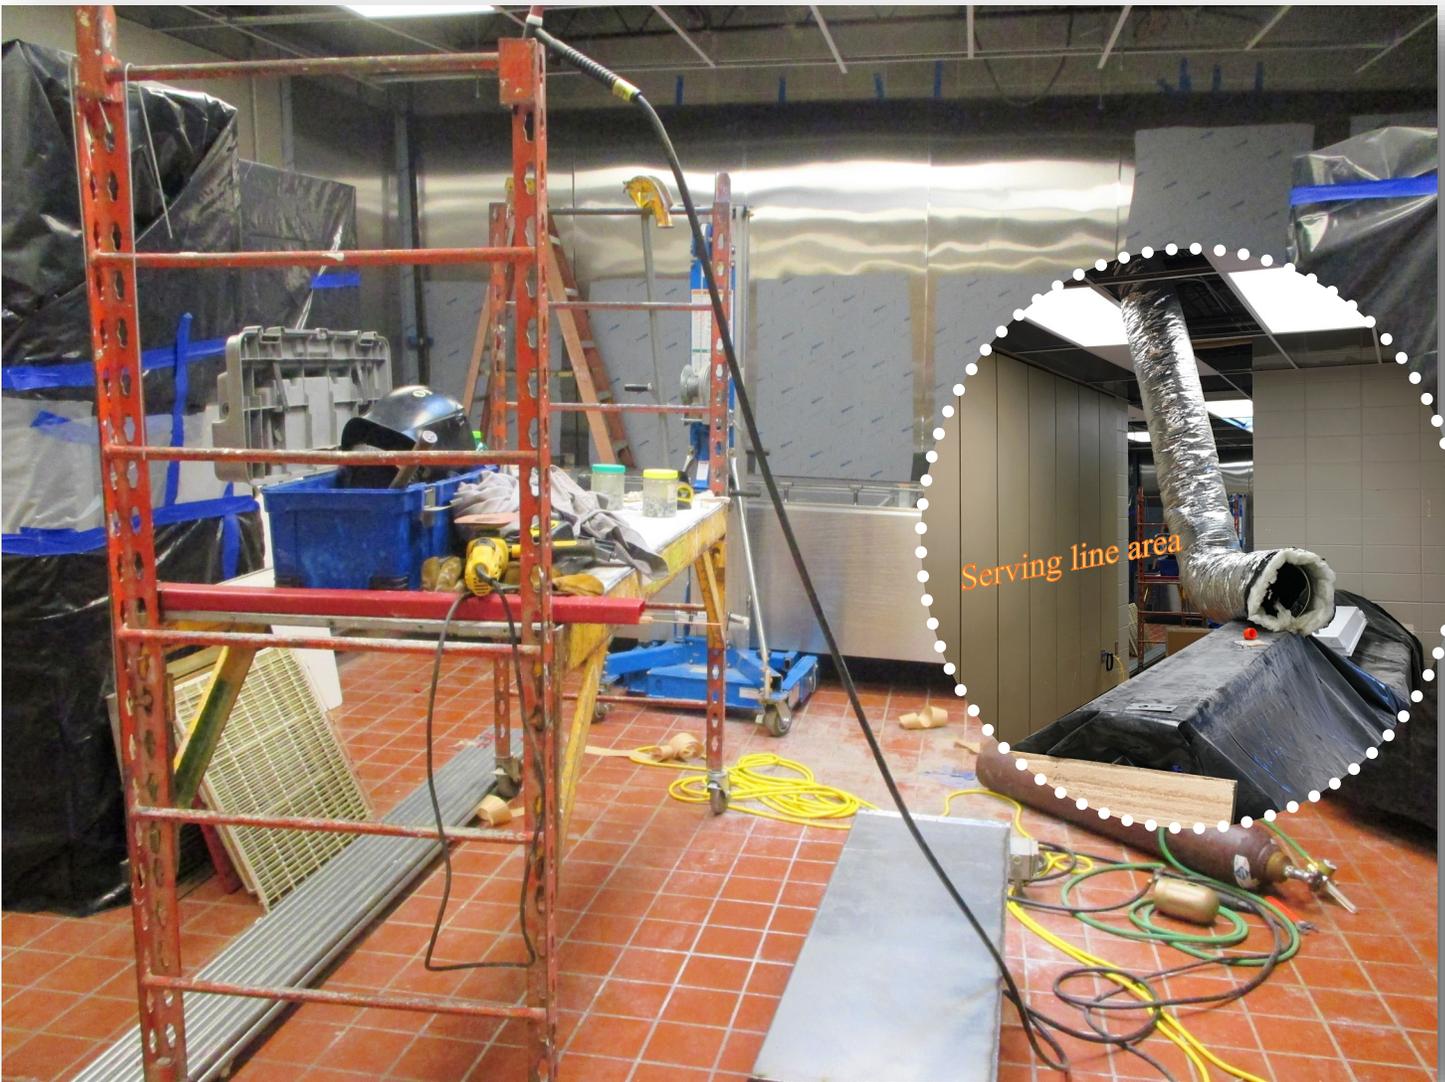

Fellowship Hall

